ID	Task Name	Duration	Start	Finish	Resource Names
1	Demo and prep sw replacement at STA 1302+10 RT, move meter behind walk,	1 day	Thu 3/15/18	Thu 3/15/18	Cradar
2	set walk and curb and pour at STA 1304+33	1 day	Fri 3/16/18	Fri 3/16/18	Guido
3	Complete underground at State street intersection - pending MH approval	3 days	Tue 3/13/18	Thu 3/15/18	Cradar
4	Demo curb and sidewalk from Umpqua to State St. - north side	7 days	Mon 3/12/18	Tue 3/20/18	Cradar
5	Excavate for tree base, install root barrier and tree frame from Umpqua to State	1 day	Mon 3/19/18	Mon 3/19/18	Guido
6	Place conduit from Umpqua to State - north sic	1 day	Wed 3/21/18	Wed 3/21/18	Kunert
7	Patch curb lines on NE Calapooia where neede	2 days	Fri 3/16/18	Mon 3/19/18	Guido
8	Begin underground work at Calapooia intersection, install inlets and storm drainage, pending MH approval	5 days	Mon 3/19/18	Fri 3/23/18	Cradar
9	Auger lamp bases from tracks to Calapooia - south side	1 day	Thu 3/22/18	Thu 3/22/18	Kunert
10	Set and pour curb from Umpqua to State	3 days	Thu 3/22/18	Mon 3/26/18	Guido
11	Pour back ramps at Umpqua and State corners	2 days	Thu 3/22/18	Fri 3/23/18	Guido
12	Set and pour walks, set tree grates from Umpqua to State	2 days	Tue 3/27/18	Wed 3/28/18	Guido

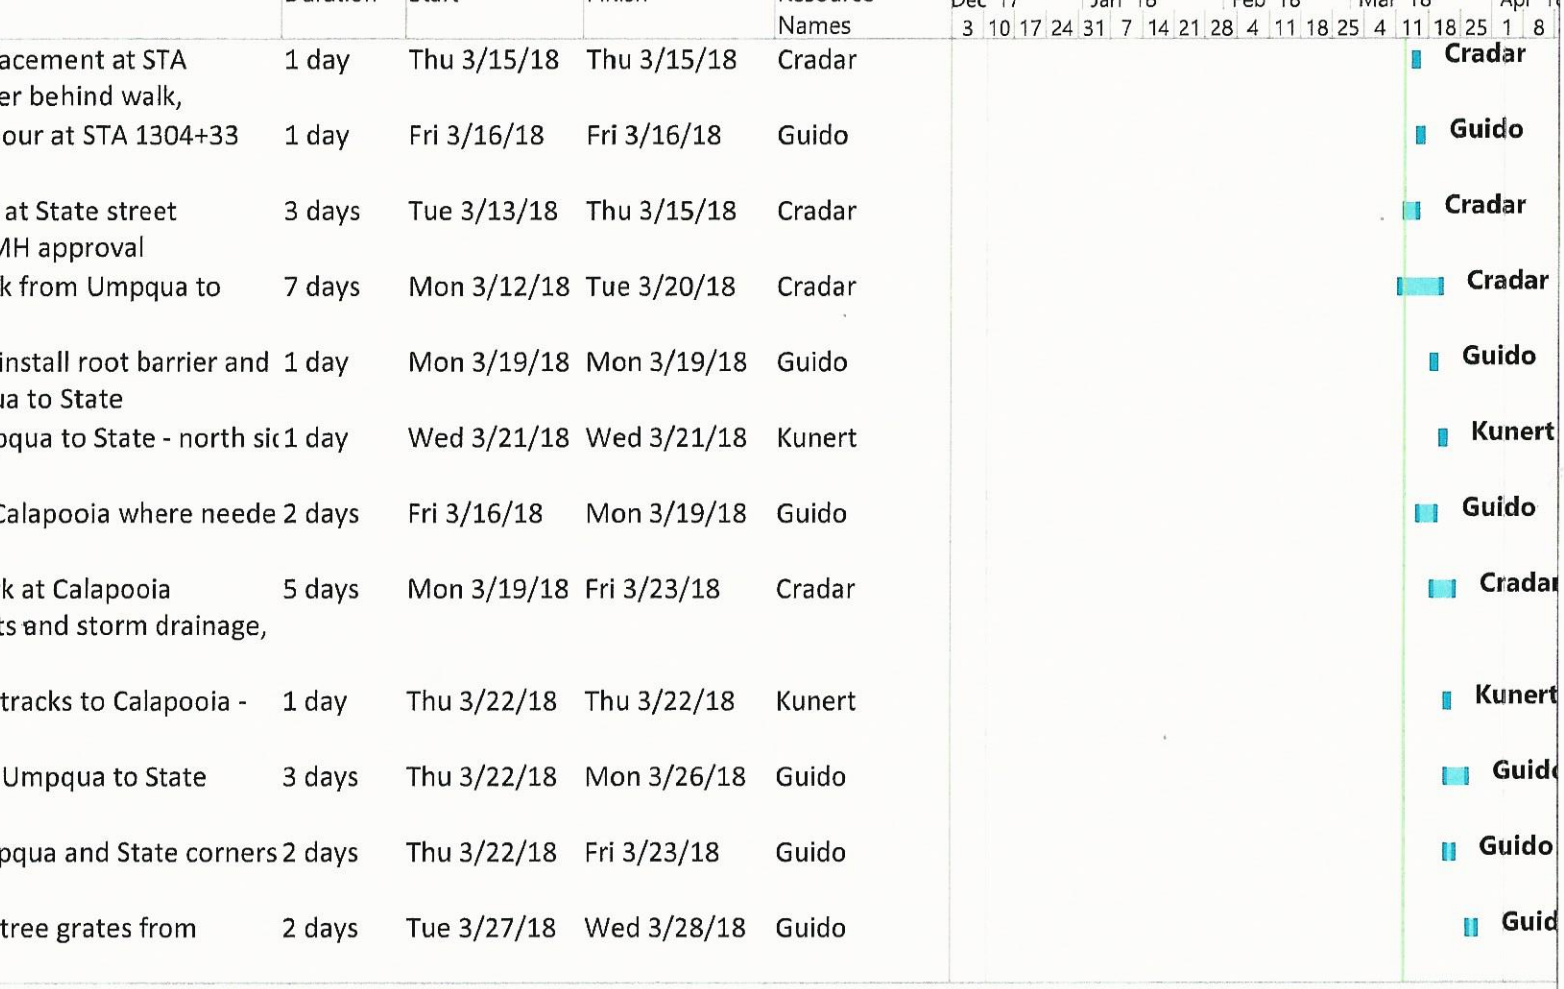

Project: CENTRAL AVE. SCHEDU
Date: Tue 3/13/18

Task	Inactive Summary	External Tasks	
Split	Manual Task	External Milestone	
Milestone	Duration-only	Deadline	
Summary	Manual Summary Rollup	Progress	
Project Summary	Manual Summary	Manual Progress	
Inactive Task	Start-only		
Inactive Milestone	Finish-only		

ID	Task Name	Duration	Start	Finish	Resource Names
13	Trench patch between Umpqua and State - north side	1 day	Thu 3/29/18	Thu 3/29/18	Guido
14	Demo from State to Calapooia - north side	5 days	Wed 3/21/18	Tue 3/27/18	Cradar
15	Place conduit from State to Calapooia - north side	1 day	Tue 3/27/18	Tue 3/27/18	Kunert
16	Pour lamp bases from tracks to Calapooia - south side	1 day	Mon 3/26/18	Mon 3/26/18	Kunert
17	Set and pour ADA ramps at Calapooia intersection	4 days	Wed 3/21/18	Mon 3/26/18	Guido
18	Form and pour curb from State to Calapooia - north side	2 days	Wed 3/28/18	Thu 3/29/18	Guido
19	Form and place sidewalk, install tree grates from State to Calapooia - north side	3 days	Fri 3/30/18	Tue 4/3/18	Guido
20	Install cyclone fencing at retaining wall	1 day	Wed 3/21/18	Wed 3/21/18	Quality Fence

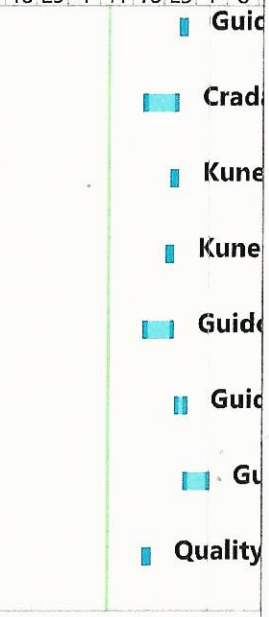

Project: CENTRAL AVE. SCHEDU
Date: Tue 3/13/18

Task
Split
Milestone
Summary
Project Summary
Inactive Task
Inactive Milestone
Inactive Summary
Manual Task
Duration-only
Manual Summary Rollup
Manual Summary
Start-only
Finish-only
External Tasks
External Milestone
Deadline
Progress
Manual Progress
